

EASTERN ARIZONA COLLEGE - MONTHLY REPORT #1

APRIL 2025

SAFETY PREDICTIVE SOLUTIONS

INSPECTIONS	OBSERVATION	INJURIES	LOST TIME	NEAR MISS
1	21	0	0	0


SCHEDULE & MILESTONES

APRIL	MAY
Over Ex Cosmo And Grey Shell	UG Electrical in Cosmo Complete
All Footings Poured for Cosmo	Cosmo Slab Rebar Install
Underground in Grey Shell Complete	Pour Concrete Slab at Cosmo
Install Storm Drain N & E of Grey Shell	West Side Sewer Tie-In
UG Plumbing in Cosmo Complete	Install Storm Drain Retention Tanks
Grade Area for Storm Drain Tanks	Pour Concrete Slab at Grey Shell

MONTHLY SUMMARY

We've made significant progress on site this month - both building's footprints are now visible and taking shape. As part of site preparation, a new storm drain system has been installed, backfilled, and extended to the newly excavated and graded area designated for the future storm drain tanks. After coordination with Graham County the existing electrical/light pole has been relocated to the Southwest of corner of the site. The Cosmetology and Grey Shell building pads have been graded and certified for underground utilities to begin. The plumbing underground work has been completed, inspected, and backfilled on both buildings. Electrical underground has been completed at the Grey Shell along with some site underground. At the end of April the electrical team began their work in Cosmo and will continue into May. Interior and perimeter concrete footings have been poured for both buildings. Since the college semester ends in early May, we will begin our utility tie-ins on the West side of the site along College Ave next month. We are excited to have a productive summer out on site!

PROGRESS PHOTOS

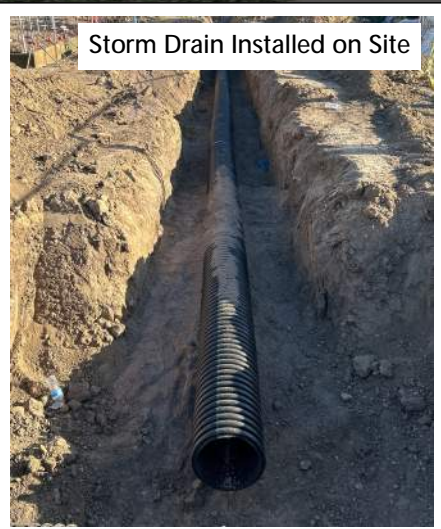

FUN FACT

A lightning bolt is five time hotter than the surface of the sun.
