



EASTERN ARIZONA COLLEGE - MONTHLY REPORT #5

AUGUST 2025

SAFETY PREDICTIVE SOLUTIONS

INSPECTIONS	OBSERVATION	INJURIES	LOST TIME	NEAR MISS
6	158	0	0	0

MONTHLY SUMMARY

We've kept up the momentum in the Cosmetology building this month. The roofing system has been installed just in time for the monsoon rains headed our way. We also installed the rooftop AC units on the high roof area. Inside the building we have framed out most of the interior walls. Electrical and plumbing in-wall rough in is going steady and will be wrapped up in September. Plumbing overhead is also mostly complete as we rolled into hanging overhead ductwork.



The main steel structure of Grey Shell is complete & the roof decking has all been installed. Roofing has started and should be complete at the very start of September. We've begun the exterior metal stud framing on that building this month as well.

Just North of Grey Shell, the storm water retention tanks are being set into place. The last pipe section of this system will be installed in September so we will be backfilling as we go and will have this portion of work all wrapped up in October.

SCHEDULE & MILESTONES

AUGUST	SEPTEMBER
Grey Shell Roof Decking Complete	Grey Shell Exterior Sheathing
Cosmo Interior Framing Ongoing	Grey Shell Roofing Install
Cosmo Roofing Complete	Grey Shell SES Install
Retention Tanks Installed	Cosmo MEP Rough In
Grey Shell Exterior Framing Started	Cosmo Interior Framing Complete
Cosmo Mech. Elect. Plumb. (MEP) Rough-In	Cosmo HVAC Units Install

PROGRESS PHOTOS

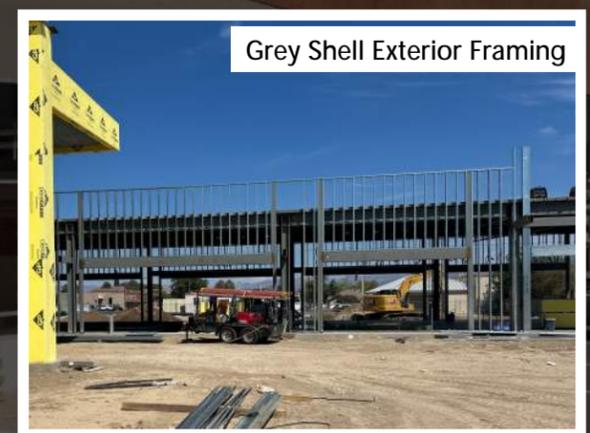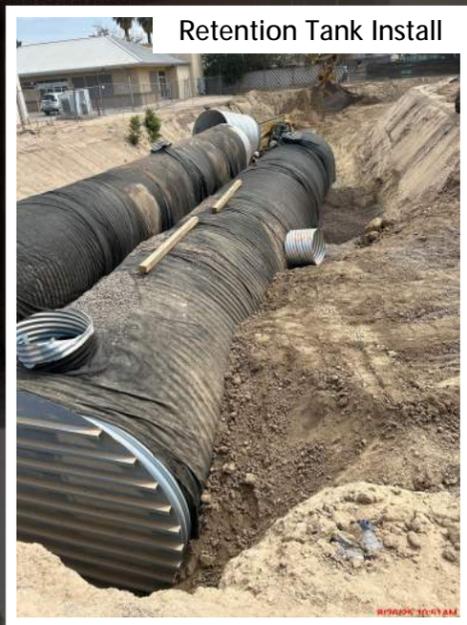

FUN FACT

From coast to coast, Australia is wider than the diameter of the Moon by approx. 350 miles

