

EASTERN ARIZONA COLLEGE - MONTHLY REPORT #12

MARCH 2026

SAFETY PREDICTIVE SOLUTIONS

INSPECTIONS	OBSERVATION	INJURIES	LOST TIME	NEAR MISS
5	97	0	0	0

MONTHLY SUMMARY

The Cosmetology building is coming closer and closer to the finish line as March has brought a lot of progress with the interior finishes. The millwork and countertops in all areas has been installed leaving only a few items to be installed. The final coat of paint has been applied throughout, wall protection and signage has also been installed. With finishes at this point, we have moved forward with laying in plumbing fixtures in all salons, classrooms, and restrooms.

The exterior of Grey Shell is complete, as such, the remaining work is taking place within the RMC Clinic. The overhead electrical system is complete, including overhead transformers, allowing us to begin prepping pathways from the high volts panels into the local panels inside of the clinic.

The landscaping is nearly complete throughout the site, decomposed granite and plants have been laid into all planters. We are also prepping the subgrade in the courtyard and south of Cosmo for the installation of landscaping pavers. Installation will take place in April.

FUN FACT

A cargo ship lost a container filled with 28,000 rubber ducks in 1992 scattering them in the ocean. These ducks are still being recovered to this day

SCHEDULE & MILESTONES

March
Cosmo Flooring & Base
Cosmo Solid Surface Countertops
Cosmo Gas Meter Install
RMC Ceiling Grid
Landscaping
Off-Site Paving

April
Cosmo Wall Coverings
Cosmo Furniture Install
RMC Clinic Light Fixture Install
RMC Clinic Finish Overhead MEP
Landscaping Pavers
Asphalt Paving

PROGRESS PHOTOS


Landscaping & Asphalt Patchback W Side of Site



Restroom Partitions



Landscaping in Planters & Prep for Pavers

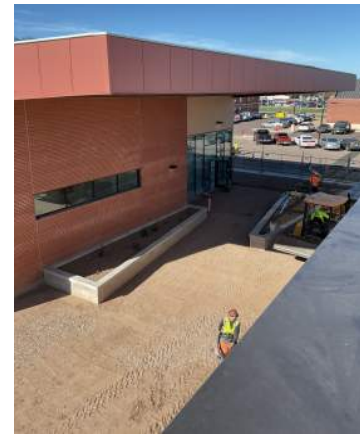

Salon Light Fixtures



Aerial Drone Photo of Site



Practice Salon

