EASTERN ARIZONA COLLEGE - MONTHLY REPORT #8

November 2025

SAFETY PREDICTIVE SOLUTIONS

INSPECTIONS	OBSERVATION	INJURIES	LOST TIME	NEAR MISS
5	132	0	0	0

MONTHLY SUMMARY

November has brought some exciting milestones for the Cosmetology building. The exterior brick veneer is complete and the storefront systems are following close behind. Within the building, the walls have been textured allowing us to move forward with painting and installing ceiling grid. We are installing the last of the conduit pathways in preparation of installing the electrical panels. Over at the Grey Shell/RMC Clinic building, the walls for the clinic are fully framed out. We are finishing up the plumbing, electrical, and mechanical rough in for both in walls and above ceiling. With the brick veneer complete at Cosmo, we have starting on the veneer for the Grey Shell.

For the site, the backfill of the storm water retention tanks is complete. Grading has begun around the entire site, we are making progress on the north parking lot and prepping the east side of the Cosmo to pour curbing and equipment pads for the new transformer and SES.

With the progress made thus far, we are on track to have this project complete prior to the start of the Fall 2026 semester.

FUN FACT

The International Space Station is the third brightest object in the sky after the sun and moon.

SCHEDULE & MILESTONES

November
Cosmo Texturing and Paint
Cosmo Brick Veneer Complete
RMC Clinic MEP Rough In Complete
Rough Grading Around Cosmo
Grey Shell Exterior Door Frames Install
Grey Shell Storefront Install

December
Cosmo Metal Paneling
Curbing at North Parking Lot
Grey Shell Brick Veneer
Grey Shell Storefront
Cosmo Concrete Floor Grinding
Pull Wire in Cosmo

PROGRESS PHOTOS

Cosmo Drywall Texture

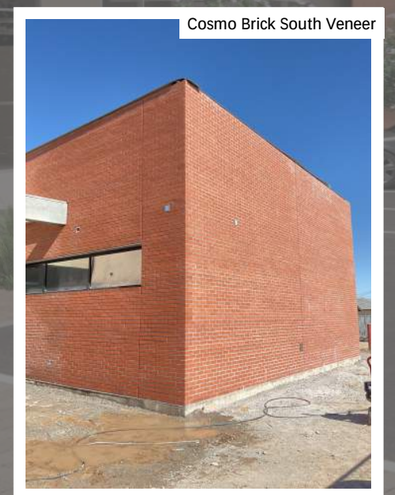
Cosmo Brick South Veneer

Cosmo Storefront Nearing Complete

Ceiling Grid Starting

Aerial Drone Photo of Site

SPS+ ARCHITECTS

EASTERN ARIZONA COLLEGE
